


Appendix E – Governance

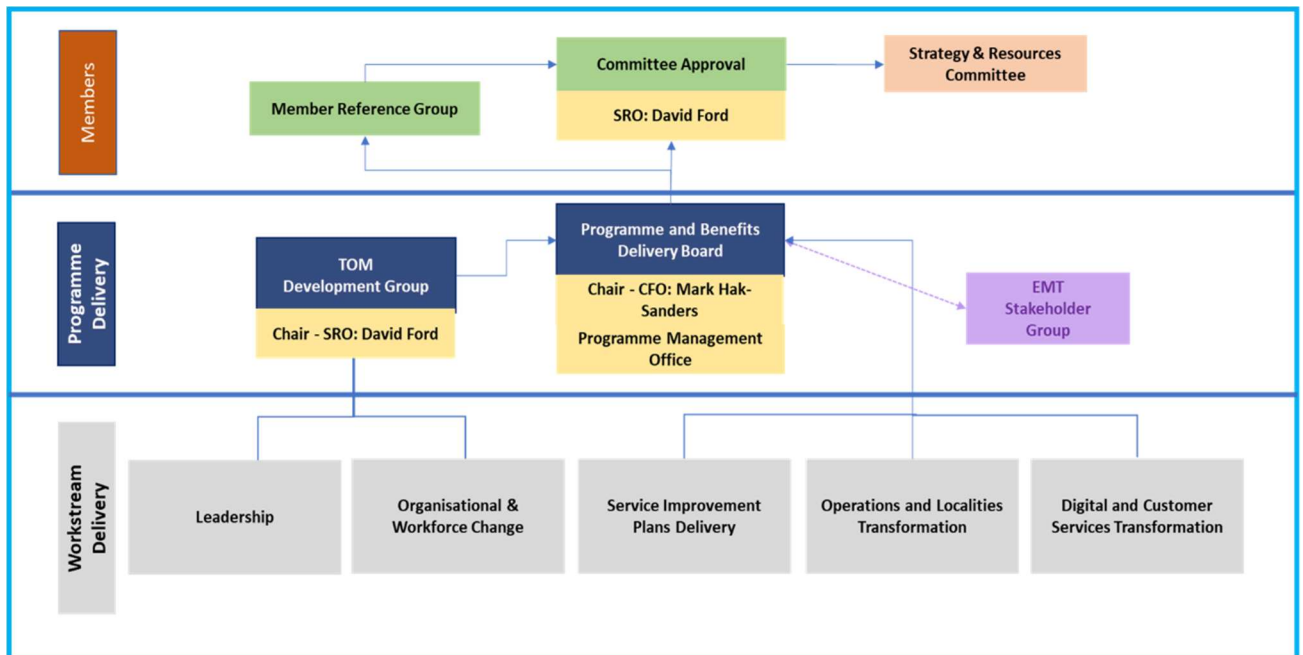

1 Member level

Formal oversight of the FTP and decision making will continue to be through the Strategy & Resources Committee, with individual committees making decisions for the services within their remit.

Alongside the formal Committee process, oversight of progress will be through the Member Reference Group. This includes the Leader and Deputy Leader of the Council, the Chair of Strategy and Resources Committee and representatives from each of the political groupings.

Wider Member engagement will continue to be undertaken on specific topics with regular progress updates provided to all Members.

2 Programme Level

At programme level, delivery of the FTP and the associated savings and benefits will be through the Programme Benefits and Delivery Board, chaired by the Chief Finance Officer and supported by the Programme Management Officer. This Board has overall accountability for delivery of the programme.

A key principle of the FTP is to ensure that the management team and Heads of Service (HOS) lead and own the delivery of changes in their service and the associated savings. HOS are directly responsible individually for:

- development of the business case for their service
- Identification of savings and other linked benefits
- development of the delivery plan for their service
- Identification of key risks and issues and their mitigation

In support of the Programme Delivery Board, HOS are collectively accountable (as the EMT) for overall progress, holding each other to account for delivery of the programme, communicating key messages and ensuring effective engagement with Council staff.

The Target Operating Model Development Group (TOMDG) oversees the development of the Leadership and Organisation Change workstreams and the change control process for the FTP. Once changes are formally approved, these will come under the remit of the PDB to ensure their delivery.

3 Workstream / Project Level

There are 5 key workstreams which support the delivery of the overall programme objectives. Due to their significance and complexity, this will include dedicated Project Boards to oversee delivery of:

- Digital and Customer Services Transformation
- Operations and Localities Transformation

Delivery of the other workstreams will be managed through the Programme Management Office with project management and other support provided where this is required to ensure delivery. Support to the Service Improvement Plans workstream will be provided on an agile basis with programme resources prioritised according to need / risk. This will be subject to ongoing review through the Programme and Benefits Delivery Board.
